
Free, open-source agent skill

Consulting decks from your files

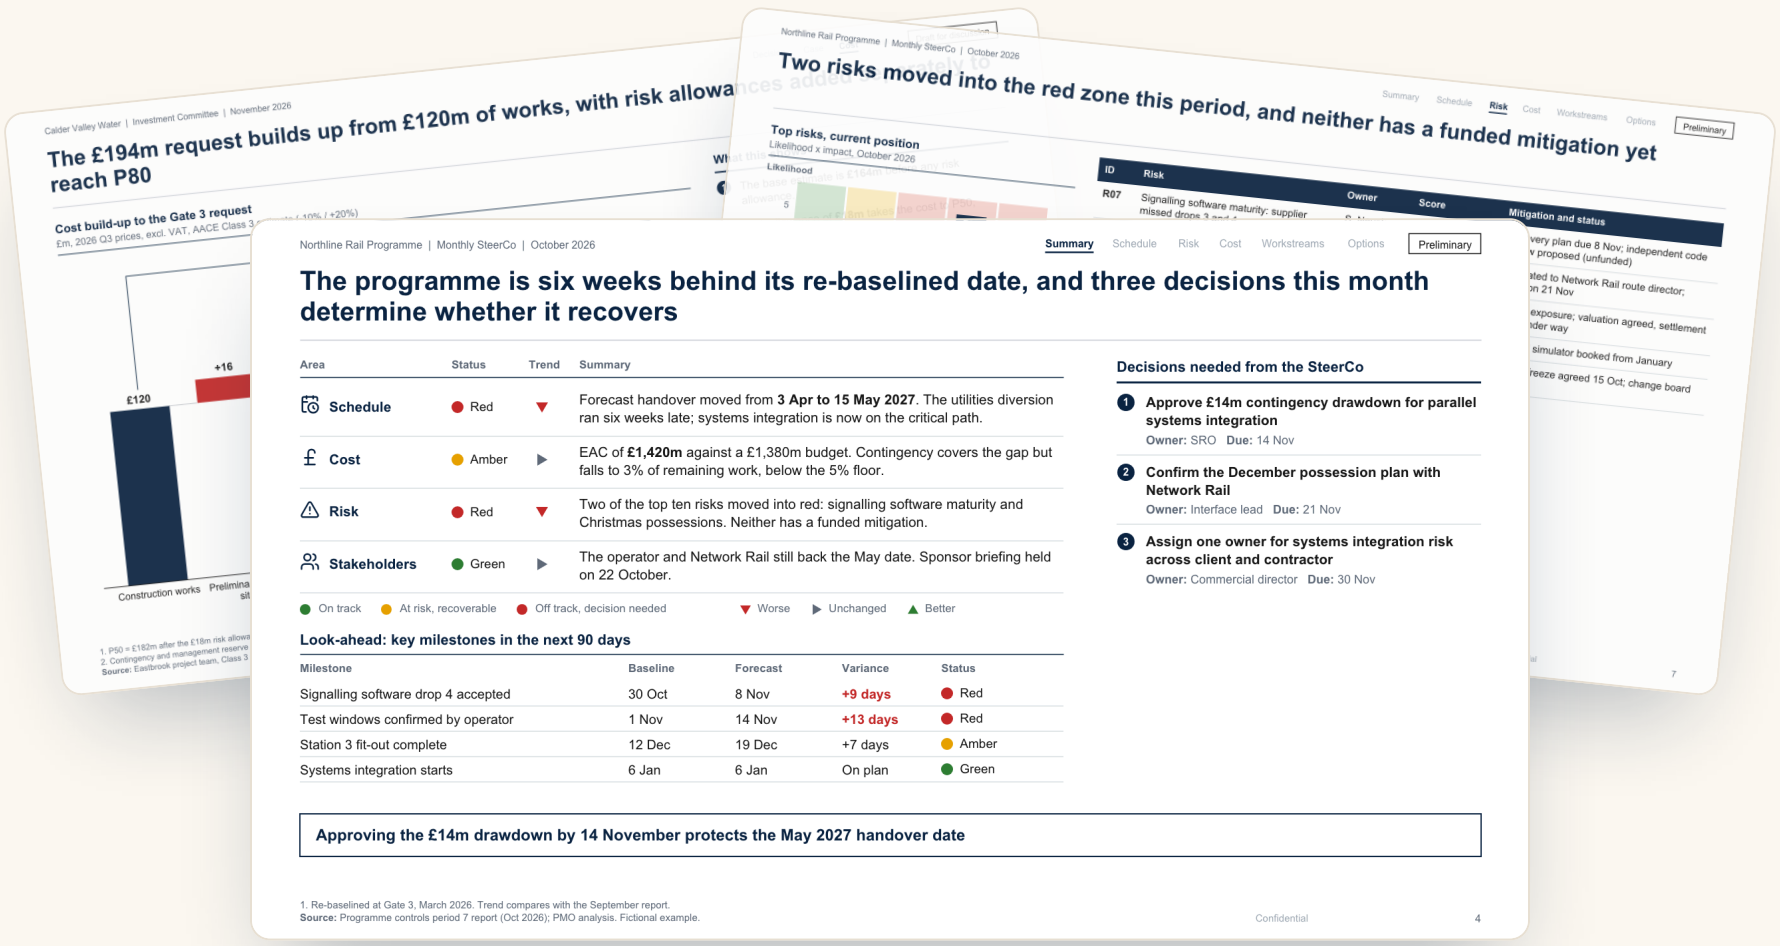

IN `notes.vtt` `schedule.xer` `risks.xlsx` `template.potx`

OUT **PPTX** **PDF** **HTML** that match, on your template

Ali Lari.

Swipe →

It reads before it asks

1 **Reads your files**

Meeting notes, transcripts, the P6 or MS Project schedule, registers in Excel, last month's deck.

2 **Plays back, then asks 3 to 5 questions**

Each comes with a default. It always covers the decision, who's in the room, and pre-read or presented.

3 **You approve the titles first**

Read only the titles and you get the story. Then it fills the slides.

4 **Builds, then checks its own work**

Every number traces to a file. PowerPoint, PDF and HTML come from one layout, so they match.

A SteerCo pack, decisions first

Status, decisions needed and the 90-day look-ahead

Northline Rail Programme | Monthly SteerCo | October 2026

Summary | Schedule | Risk | Cost | Workstreams | Options | Preliminary

The programme is six weeks behind its re-baselined date, and three decisions this month determine whether it recovers

Area	Status	Trend	Summary
Schedule	Red	▼	Forecast handover moved from **3 Apr to 15 May 2027**. The utilities diversion ran six weeks late; systems integration is now on the critical path.
Cost	Amber	▶	EAC of **£1,420m** against a £1,380m budget. Contingency covers the gap but falls to 3% of remaining work, below the 5% floor.
Risk	Red	▼	Two of the top ten risks moved into red: signalling software maturity and Christmas possessions. Neither has a funded mitigation.
Stakeholders	Green	▶	The operator and Network Rail still back the May date. Sponsor briefing held on 22 October.

● On track ● At risk, recoverable ● Off track, decision needed ▼ Worse ▶ Unchanged ▲ Better

Look-ahead: key milestones in the next 90 days

Milestone	Baseline	Forecast	Variance	Status
Signalling software drop 4 accepted	30 Oct	8 Nov	+9 days	Red
Test windows confirmed by operator	1 Nov	14 Nov	+13 days	Red
Station 3 fit-out complete	12 Dec	19 Dec	+7 days	Amber
Systems integration starts	6 Jan	6 Jan	On plan	Green

Decisions needed from the SteerCo

1. **Approve £14m contingency drawdown for parallel systems integration**
   Owner: SRO **Due:** 14 Nov
2. **Confirm the December possession plan with Network Rail**
   Owner: Interface lead **Due:** 21 Nov
3. **Assign one owner for systems integration risk across client and contractor**
   Owner: Commercial director **Due:** 30 Nov

Approving the £14m drawdown by 14 November protects the May 2027 handover date

1. Re-baselined at Gate 3, March 2026. Trend compares with the September report.
Source: Programme controls period 7 report (Oct 2026); PMO analysis. Fictional example.

Confidential 4


The schedule: baseline against forecast, with the slip

Northline Rail Programme | Monthly SteerCo | October 2026

Summary | Schedule | Risk | Cost | Workstreams | Options | Preliminary

Systems integration is now the critical path; handover holds only if test windows are confirmed by 14 November

Integrated schedule, baseline vs current forecast
Level 2 programme schedule, October 2026 to June 2027

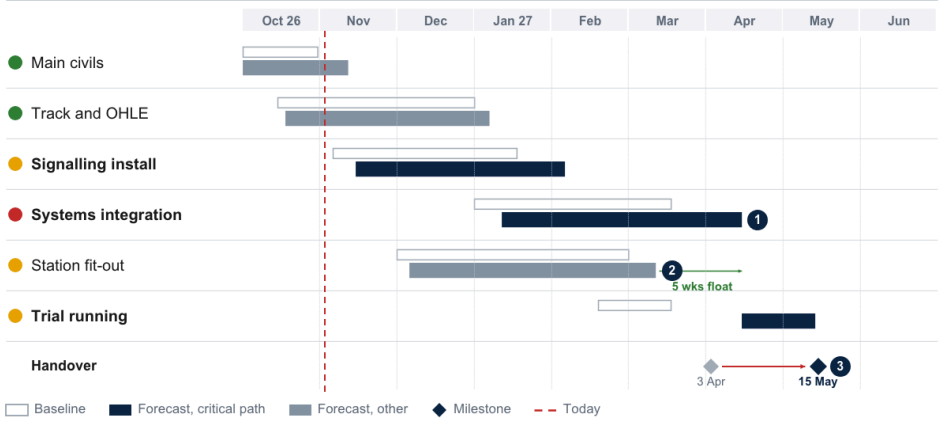

What the schedule shows

1. Systems integration now drives handover. Its finish has slipped four weeks, to mid-April.
2. Station fit-out has five weeks of float, so it can move to make room for testing.
3. The 15 May date holds only if the operator confirms test windows by 14 November.

Next steps

- Operator to confirm test windows (14 Nov)
- Delivery partner to issue a resequenced fit-out plan (21 Nov)
- PMO to re-run schedule risk analysis on the new logic (28 Nov)

1. Baseline is the Gate 3 re-baseline (March 2026). Float is total float on the Level 2 schedule.
Source: Programme controls period 7 report (Oct 2026); PMO analysis. Fictional example.

Confidential 6

A Gate 3 paper with its P80

Cost build-up, with the estimate class in the unit line

Calder Valley Water | Investment Committee | November 2026


Decision Case **Cost** Risk

Draft for discussion

The £194m request builds up from £120m of works, with risk allowances added separately to reach P80

Cost build-up to the Gate 3 request

£m, 2026 Q3 prices, excl. VAT, AACE Class 3 estimate (-10% / +20%)

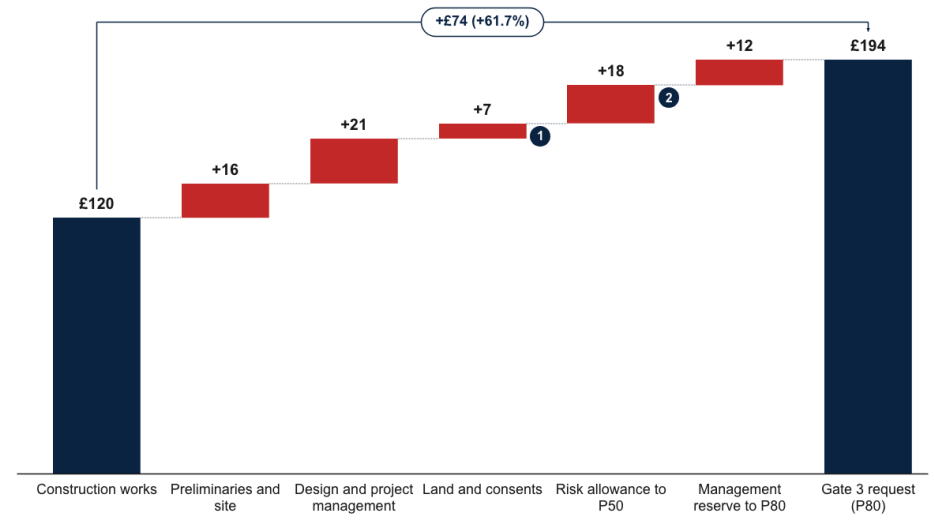

What this shows

1. The base estimate is **£164m** before any risk allowance.
2. Risk allowance of **£18m** takes the cost to P50, £182m.
3. The extra **£12m** reserve lifts confidence from 50% to 80%.

1. P50 = £182m after the £18m risk allowance. Management reserve of £12m takes the total to P80.
2. Contingency and management reserve are held by the Investment Committee, not the project.

Source: Eastbrook project team, Class 3 estimate and QRA, October 2026. Fictional example.

Confidential 5

The QRA: P50, P80 and what the budget really covers

Calder Valley Water | Investment Committee | November 2026

Decision Case Cost **Risk**

Draft for discussion

At £194m the budget has an 80% chance of holding, against 50% at the £182m base case

Probability that outturn cost is at or below

£m, 2026 Q3 prices, excl. VAT



Implication for Gate 3

1. Funding at P80 meets the Committee's confidence policy.
2. The largest drivers are ground conditions and membrane supply lead times.

1. Monte Carlo cost risk analysis, 5,000 iterations, risk register version 7 dated 9 October 2026, with correlation between ground and civils risks.

Source: Eastbrook project team, Class 3 estimate and QRA, October 2026. Fictional example.

Confidential 6


Market entry. Operating model.

Where to play: attractiveness against ability to win

Tidewell Cold Chain | Board strategy session | November 2026

Summary Market **Where to play** How to enter Decision Draft for discussion

Food service combines strong growth with our best chance of winning; pharma is attractive but needs licences we lack

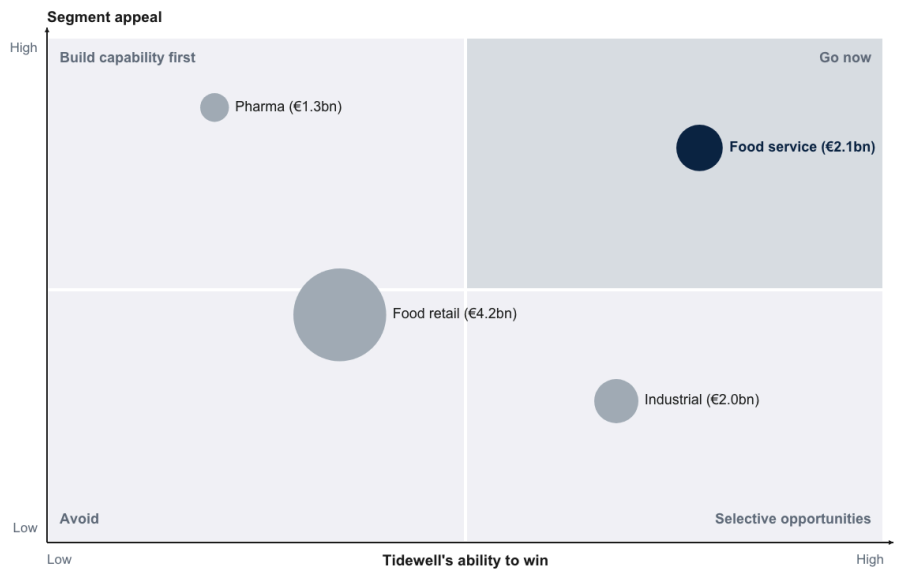

Reading the matrix

1. Food service is the only segment in the top right.
2. Pharma needs good distribution practice certification, which takes about 24 months to obtain.

1. Bubble size is 2026 segment size. Scores are the strategy team's judgement from 14 expert interviews and a review of Tidewell's capabilities.
Source: Nordic Cold Chain Observatory, Market Report 2026 (fictional); Tidewell strategy team analysis. Fictional example.

Confidential 5

Today against the target model, dimension by dimension

Calder Valley Homes | Board and Executive Team | November 2026

Summary Principles **Design** Decision rights Transition Draft for discussion

Today nine directorates share tenant outcomes; the target model gives each outcome one owner

	Today	From 1 July 2027
Structure	Nine directorates, each with its own management team	**Five** divisions: homes, property, finance, people, digital
Layers	Six layers from Chief Executive to front line	**Five** layers
Span of control	Average of 4.1 reports per manager	Average of **7.0** reports per manager
Repairs	Three directorates touch each job; 23 days to close on average	One owner end to end; target **14** days
Systems	Four housing systems that do not share data	One housing system and one weekly dashboard

1. Spans and layers from the HR system, October 2026. Repairs times from the repairs system, January to September 2026.
Source: Calder Valley Homes HR and finance data, October 2026; staff workshops; transformation team analysis. Fictional example.

Confidential 4


Built on your own template

House style

Two risks moved into the red zone this period, and neither has a funded mitigation yet

Top risks, current position

Likelihood x impact, October 2026

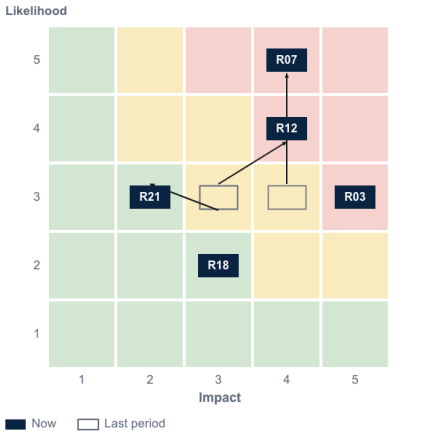

ID	Risk	Owner	Score		Mitigation and status
R07	Signalling software maturity: supplier missed drops 3 and 4	S. Novak	12 → 20	▲	Recovery plan due 8 Nov; independent code review proposed (unfunded)
R12	Christmas possessions: 3 of 5 weekends unconfirmed	Interface lead	9 → 16	▲	Escalated to Network Rail route director; decision 21 Nov
R03	Utilities diversion claims from main contractor	R. Dube	15 → 15	▶	£6-9m exposure; valuation agreed, settlement talks under way
R18	Driver training capacity for trial running	K. Ahmed	6 → 6	▶	Second simulator booked from January
R21	Late design changes at Station 3	A. Silva	9 → 6	▼	Design freeze agreed 15 Oct; change board in place

▲ Score rising ▶ Unchanged ▼ Score falling

1. Score = likelihood x impact on a 5 x 5 scale. Red is 15 or more; amber 8 to 14; green 7 or less.
Source: Programme controls period 7 report (Oct 2026); PMO analysis. Fictional example.


Your .potx: your master, fonts and colors

Preliminary

Two risks moved into the red zone this period, and neither has a funded mitigation yet

Top risks, current position

Likelihood x impact, October 2026

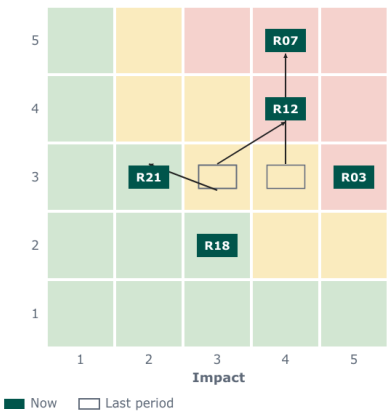

ID	Risk	Owner	Score		Mitigation and status
R07	Signalling software maturity: supplier missed drops 3 and 4	S. Novak	12 → 20	▲	Recovery plan due 8 Nov; independent code review proposed (unfunded)
R12	Christmas possessions: 3 of 5 weekends unconfirmed	Interface lead	9 → 16	▲	Escalated to Network Rail route director; decision 21 Nov
R03	Utilities diversion claims from main contractor	R. Dube	15 → 15	▶	£6-9m exposure; valuation agreed, settlement talks under way
R18	Driver training capacity for trial running	K. Ahmed	6 → 6	▶	Second simulator booked from January
R21	Late design changes at Station 3	A. Silva	9 → 6	▼	Design freeze agreed 15 Oct; change board in place

▲ Score rising ▶ Unchanged ▼ Score falling

1. Score = likelihood x impact on a 5 x 5 scale. Red is 15 or more; amber 8 to 14; green 7 or less.
Source: Programme controls period 7 report (Oct 2026); PMO analysis. Fictional example.

What it catches before you send

- Titles that are topics, not takeaways
- Numbers with no source (file, row or speaker)
- Waterfalls that don't add up
- A RAG status with no definition or evidence
- A gate paper with no estimate class or P80
- A status report with no decisions page
- "Leverage", "holistic", "unlock" and the rest

36 deck types across four practices

PMO

Monthly status report
SteerCo pack
Risk review
IV&V and health checks
Go-live readiness

CAPITAL PROJECTS

Gate paper
Independent cost review
QRA results
Delivery model
Recovery plan

STRATEGY

Strategic diagnostic
Growth strategy
Market entry
Due diligence summary
Board strategy update

MANAGEMENT

Cost review
Operating model
Transformation roadmap
Post-merger integration
Service review

Free and open source (MIT). Runs in Claude Code, Codex, Gemini CLI, Cursor and about ten other agents. Repo link in the post.
